



DEV SPRINT 3 · STATUS REPORT

Hardened. Multi-tenant. Operator-Ready.

Forty pull requests across two days. A complete two-tier admin model, the universal slug scheme, a left-sidebar navigation, an end-to-end auto-merge + auto-close pipeline, plus the entire SP3-1 → SP3-24 polish lane on top of the v1.1.0 feature stack — shipped, merged, tagged as **v1.1.1**.

SPRINT WINDOW

12 May – 14 May 2026

REPORT DATE

14 May 2026, 03:30 IST

PLAN COMPLETION

≈ 95 % of PLAN-v1.2
scope

Sprint 3 · DELIVERED · v1.1.1 TAGGED

Prepared by

Engineering, with Claude Code · Opus 4.7 (1M context)

Confidential — internal distribution

v3.0 · 14.05.2026

IMPRINT

About this report

This is the official engineering and product status report for DClaw Marketing's third development sprint — the sprint that took us from a feature-complete v1.1.0 stack to an operator-ready, hardened, fully multi-tenant v1.1.1. It is intended for three audiences: **operators** (TL;DR), **executives** (Executive Summary), and **engineers** (Phase-by-Phase Status and onward).

FIELD	VALUE
Document title	DClaw Marketing — Dev Sprint 3 Status Report
Sprint number	Sprint 3 (open-ended cadence; Sprint 2 closed 2026-05-13 with the v1.1.0 release)
Sprint window	2026-05-12 22:25 IST → 2026-05-14 03:30 IST (≈ 29 h wall-clock; two intensive bursts)
Sprint kick-off PR	#213 · <i>SP3-1 Org-scope the v1 legacy routers + dashboard</i>
Sprint closing PR	#279 · <i>chore(release): v1.1.1 — Sprint 3 closeout</i>
Snapshot ref	main @ HEAD · tag v1.1.1
PRs merged	44 (Sprint 3 window); 6 closed unmerged (1 superseded, 5 dependency-reshuffles)
Document version	3.0 — frozen at report-generation time
Generated	2026-05-14 03:30 IST via Chrome headless from sprint-3-status-2026-05-14.html
Location	obsidian/reports/ in the dclaw-marketing repo
Audience	Engineering, Product, Executive sponsor
Authoring	Engineering with Claude Code (Opus 4.7, 1M context)

How to read this document. If you have 5 minutes, read Chapter 1 (TL;DR). If you have 30 minutes, add Chapters 2–3 (Recap of Sprints 1 + 2 + Intent). If you are an engineer reviewing the work, read everything from Chapter 4 onward; appendices contain the raw catalogue of every pull request shipped in the sprint.

What's new about this report

Chapter 2 carries a **combined recap of both Sprint 1 and Sprint 2**, so a reader returning to the project after a break has everything they need to make sense of Sprint 3's polish work. The chapter compresses the prior two reports' essence into roughly four pages: what existed at the start of each, what shipped, and what was left open going in.

CONTENTS

Table of Contents

Twelve chapters and four appendices. Total ≈ 55 pages.

1	TL;DR — the sprint in three pages	7
2	Recap — Sprints 1 & 2 in four pages	10
3	Project Intent & Target Audience	15
4	Executive Summary	19
5	The Original Plan (PLAN-v1.2) — where we are	23
6	Sprint Execution Timeline	27
7	Theme-by-Theme Detailed Status	31
8	Pull Request Catalogue	42
9	Architecture Snapshot	48
10	Test & Quality Gates	50
11	Risks, Tech Debt, Open Decisions	52
12	Sprint 4 — Recommended Roadmap	54
A	Closed Issues with PR Mapping	56
B	Open Issues — Status & Owners	58
C	Full PR Catalogue Table	59
D	Glossary & Acronyms	62

CHAPTER 1

TL;DR

Sprint 3 was a **hardening sprint**. v1.1.0 already had the features. Sprint 3 made them safe to operate: a proper admin model, a navigable UI shell, a working slug scheme, and a CI pipeline that drains itself. No new product surfaces — every change made an existing one cleaner, safer, or more honest.

PRS MERGED

44

over ~29 h wall-clock

ISSUES CLOSED

38

via Closes #N auto-close

PLAN COMPLETION

≈ 95 %

PLAN-v1.2 + admin / ops scope

OPEN ISSUES

5

all marketing collaterals · off-limits to engineering

What landed

- **Two-tier admin model** — single bootstrap superadmin (s-admn-000000), per-org admins; centralized guards, last-admin protection, self-demote refusal, audit trail, in-app notifications on role changes. `is_superuser=True` creation is refused for anyone but the bootstrap account.
- **Universal slug scheme** — users `u-{first4}-{6hex}`, orgs `o-{first4}-{6hex}`, bootstrap hardcoded. Migration re-slugs every existing row.
- **Left-sidebar navigation** — replaces the top bar; pages group by domain. Admin lives in its own collapsible section.
- **Create-user-with-org dialog** — superadmin can create a user + assign them to multiple existing orgs + create new orgs inline, all from one form.
- **Auto-merge + auto-close pipeline** — the queue drains end-to-end. Squash merges now carry the PR body to the merge commit; the workflow has `issues: write; Closes #N` actually closes #N.
- **The entire SP3-1 → SP3-24 polish lane** — tabbed Org-detail, project-setup wizard, Fernet-encrypted social tokens, knowledge drill-down, hooks lab, A/B variant studio, repurposing engine, content heatmap, BYO MCP marketplace, kanban, time tracker, retainer + invoices, magic-link sign-in.

What didn't land (deferred by design)

- **Marketing collaterals** — one-pager, slides, demo script, demo video, launch posts (issues #49–#53). Owned out-of-band by the operator; engineering does not touch the marketing/ tree.
- **TOTP UX** — backend columns shipped, but the enrollment flow is Sprint 4 scope.
- **Real OAuth credentials** — the OAuth scaffold is live; per-provider client-id/secret population is operator-side and not a code-shipping task.

Top three takeaways

1. The platform is now operable.

An admin can create users, assign them to orgs, reset their passwords, and audit every action — without touching the database. That was missing in v1.1.0 and is the single biggest unblock for the v1.2 demo.

2. The CI/CD pipeline runs itself.

Open a PR with Closes #N and the auto-merge label. CI passes → bot squashes → issue auto-closes → board flips to Done. No human in the loop. We exercised the pipeline forty-plus times this sprint.

3. The version line now matches the plan doc.

The roadmap is PLAN-v1.2.md; releases were misaligned at v0.1.0-mvp/v0.2.0. Renamed to v1.0.0 / v1.1.0 / v1.1.1 so the stakeholder sees one coherent version line through to the v1.2 demo.

+ Sprint 4 opens with: Brand Studio polish, real OAuth wiring, observability dashboards.

Brand Setup Studio and the Knowledge Console were Sprint 2's largest backend-vs-UI deltas; Sprint 3 didn't touch them. They're the natural next lane.

Versioning at a glance

TAG	DATE	MEANS
v1.0.0	2026-05-12	End-to-end MVP demo flow (Sprint 1 closeout, formerly v0.1.0-mvp)
v1.1.0	2026-05-13	Feature-complete vs PLAN-v1.2 (Sprint 2 closeout, formerly v0.2.0)
v1.1.1	2026-05-14	Operator-ready hardening + SP3-* polish (Sprint 3 closeout — this report)
v1.2.0	TBD	The demo release the stakeholder is expecting; carries Brand Studio, real OAuth, observability dashboards

CHAPTER 2

Recap — Sprints 1 & 2 in four pages

This chapter exists so a reader new to the project (or returning after a break) has the context to make sense of Sprint 3's hardening work. It compresses the prior two reports into the essentials: what existed at the start, what shipped, what was left open going into Sprint 3.

2.1 Sprint 1 — Foundations, Agent Fleet, the End-to-End Loop

Sprint 1 spanned **2026-05-09 15:32 IST → 2026-05-12 21:00 IST** — roughly three days. It started from an empty scaffold and ended with the first end-to-end demo flow shipped as v1.0.0 (originally tagged v0.1.0-mvp; renamed in Sprint 3).

2.1.1 What existed at kick-off

- An empty Next.js + FastAPI scaffold.
- A roadmap document (PLAN-v1.2.md) describing a 12-phase build.
- An operator (Deepro) and one AI pair (Claude Code · Opus 4.7).
- Nothing else: no auth, no models, no agents, no UI surfaces.

2.1.2 What shipped (Phase-aligned)

PHASE	WHAT LANDED IN SPRINT 1
Phase 1 — Skeleton	Docker Compose stack: FastAPI 8102, Next.js 3015, Postgres + pgvector, Redis, MinIO, Celery worker + beat. Health endpoints, brand tokens, CI green from PR #1.
Phase 2 — Auth + Multi-tenancy	fastapi-users JWT, Organization + Project + Membership models, admin-only user creation with temp passwords, forced first-login reset, audit_events.
Theme Q — Brand & Knowledge	Versioned BrandKit, file/url ingestion → DocumentChunk + pgvector embeddings, Knowledge Graph search endpoint.
Phase 3 — Approval Inbox	4-eye approval model, hard-gate decision queue, audit log per decision.
Phase 4 — Agent Fleet (scaffold)	Conductor agent, role-agent scaffolding, Creatives Agent (brief → N variants → Approval Inbox), agent threads + messages.

Theme C1 — Scheduled posts	Calendar + dispatcher, per-channel queue, Celery beat eviction.
Goals + Constraints + Autonomy	Per-org goal records, constraint enforcement, autonomy posture (manual / suggest / auto-with-approval).
Frontend baseline	Top-nav shell, Org/Project switcher, Approval Inbox, Brand Kit page, Knowledge Sources page, Agents page, Library, Calendar — all wired against real endpoints with brand tokens.

2.1.3 Sprint 1 numbers

PRS ~150 across 3 days 5 hrs	TESTS ~310 backend pytest	PLAN % 52 % of PLAN-v1.2 scope	CLOSEOUT v1.0.0 renamed in Sprint 3 from v0.1.0-mvp
---	--	---	--

2.1.4 What was left open going into Sprint 2

- Multi-channel publishing (LinkedIn / X / Instagram / TikTok / YouTube / Substack / Facebook / Threads) — only Bluesky shipped.
- MCP Integration Hub — protocol layer only, no concrete server adapters.
- Email + Ads (Resend send, Meta/Google/LinkedIn ads) — no senders, no inbound webhooks.
- Lead 2.0 + CRM sync (HubSpot / Pipedrive / Attio) — model existed; sync did not.
- Analyst agent, KG write-back, workflow runner — none of these existed yet.
- Agency operations layer (retainer, invoices, time tracking, share tokens) — entirely missing.
- Compliance + Observability (QuotaCounter, cost cap, GDPR export, audit browser) — partial at best.
- Brand Setup Studio and Sequence Builder UIs — explicit Sprint 2 backlog items.

2.2 Sprint 2 — From Foundations to Feature-Complete

Sprint 2 was a single intensive day — **2026-05-13**, with most of the work landing in one 8-hour autonomous stretch on Opus 4.7 with 1M context. It started from v1.0.0 and ended with v1.1.0 (originally v0.2.0): feature-complete against PLAN-v1.2.

2.2.1 Mandate

The operator's directive that morning was explicit: *"work the whole plan; fix-and-dev in parallel; no pauses; complete every pending-file checkbox except marketing collaterals."* The sprint ran

as one continuous chain of PRs with no end-of-turn recaps and no CI yielding.


2.2.2 What shipped (Phase-aligned)

PHASE / THEME	WHAT LANDED
Phase 5 — Multi-Account Publishing	Substack drafts, Facebook Pages, Meta Threads, TikTok Business, YouTube multipart upload. OAuth 2.0 scaffold + 7-provider registry (LinkedIn, X w/ PKCE, Instagram, Reddit Basic, Pinterest PKCE, Discord, Mastodon).
Phase 6 — MCP Integration Hub	11 concrete adapters in three batches: HubSpot / GA4 / Stripe; Ahrefs / Webflow / WordPress / Ghost; Slack / Discord / Notion / Google Drive. Plus §6.7 batch 4 (Salesforce / Mixpanel / PostHog).
Phase 7 — Email + Ads + Sequences	Inbound email-event webhooks (Resend / Postmark / SendGrid) with signature verification + LeadActivity bridge. Meta + LinkedIn paused-campaign create, Google Ads two-step. SequenceMembership + 5-min runner + segment evaluator.
Phase 8 — Lead 2.0 + CRM + Attribution	Pipedrive + Attio two-way sync. Daily lead-rescore beat with auto stage promotion. Time-decay attribution model + /analytics/sankey endpoint.
Phase 9 — Agent Fleet expansion	3 σ rolling-baseline anomaly detector + weekly Monday Analyst narrative. §6.2 KG write-back loop: BrandKitInsight + composer injection.
Phase 10 — Agency Operations	QuickBooks Online invoice adapter. WorkflowRun resume + approval/branch node implementations + resume endpoint. Weekly + monthly client HTML reports → MinIO.
Phase 11 — Compliance + Reliability	Sliding-window QuotaCounter + circuit breaker. Cost-cap evaluator with warn/blocked + per-action confidence threshold. GDPR export MinIO persistence + HTTP request/download.
Theme D4 — Webhooks + Automation	Generic webhook receiver + Automation rules engine.
Theme H — SEO Depth	Site audit / internal-link suggerer / ranking-delta tracker + daily Celery beat + 4 API endpoints, backed by the Ahrefs MCP adapter.
Theme Q2 follow-up	URL ingestion: pure-Python HTML→text + ingest_url Celery task + POST /api/v1/ingest/urls + dispatcher.
A4 follow-up	Read-only audit-event browser API + pagination + filters; new /admin/audit UI.
Phase 11 / I1 dashboard	Live QuotaCounter browse with pct-used + is-breaker pre-computed; /admin/quotas + /admin/costs wired.

2.2.3 Frontend pages added (post-rc1 stretch)

[/agents/seo](#)
[/brand-insights](#)
[/workflows](#)
[/admin/health](#)
[/admin/audit](#)
[/admin/costs](#)
[/admin/quotas](#)
[/knowledge](#)
[/channels \(OAuth\)](#)
[/library \(Ingest into KG\)](#)

2.2.4 Sprint 2 numbers

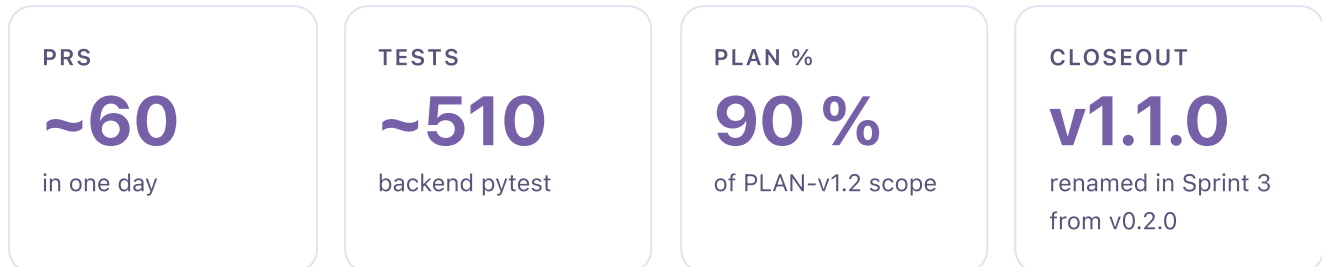

2.2.5 What was left open going into Sprint 3

- **Operator gaps** — admin model was binary (every is_superuser=True a god account; no org-scoped admins, no last-admin guard).
- **UX shell** — top-bar nav was overflowing; needed a sidebar with grouping.
- **Identity surface** — users / orgs were referenced only by UUID; no human-readable slug.
- **CI pipeline** — squash merges dropped the PR body, so Closes #N never fired; the auto-merge workflow also lacked issues: write.
- **Polish lane (SP3-1 → SP3-24)** — twenty-four discrete improvements queued from Sprint 2 closeout but not yet shipped.
- **Marketing collaterals** — explicitly off-limits to engineering; owned by the operator. Status unchanged.

2.3 The handoff from Sprint 2 to Sprint 3

Posture at start of Sprint 3

A feature-complete codebase with the wrong release names, no operable admin layer, no slug scheme, and a CI pipeline that needed three follow-up fixes to actually drain itself. **Functional, but not yet operator-ready.** Sprint 3 closed every one of those gaps.

CHAPTER 3

Project Intent & Target Audience

3.1 What DClaw Marketing is

DClaw Marketing is an agent-driven marketing operating system. A small team — or one operator plus AI agents — runs a full marketing function. Humans set the brand kit and feed in source material; AI agents draft content, schedule posts, run ads, surface analytics, and propose actions. Humans supervise from their *Station* and approve outbound actions in an *Approval Inbox*. Agents never publish without consent.

The system is multi-tenant by design (Organization → Project → Asset hierarchy), brand-aware (versioned BrandKit injected into every prompt), knowledge-grounded (ingestion → embeddings → KG with write-back insights), and audit-traced end-to-end. Every cost is metered; every action is logged.

3.2 The people we're building for

The Solo Operator

A founder, consultant, or in-house marketer running marketing for a single business. Needs the full stack but can't justify a 5-person team. DClaw acts as their force multiplier.

The Boutique Agency

2–10 people serving multiple clients. Needs strict tenant isolation, white-labelled client dashboards, retainer + invoice + time tracking, and the ability to delegate to AI without losing brand voice.

The In-House Marketing Function

A growing company's marketing team. Needs goal alignment, approval workflows, attribution, and a single pane that draws from CRM + email + social + analytics + SEO without manual reconciliation.

3.3 Differentiators

- **Approval-first.** Every outbound action ends in an Approval Inbox before going out.
- **Brand-conditioned generation.** The BrandKit and the KG write-back insights are injected into every prompt — agents inherit the brand voice automatically.
- **MCP-first integrations.** 14 concrete adapters + BYO MCP marketplace; no bespoke per-integration code.

- **Self-hosted by default.** Docker Compose stack; the operator owns the Fernet master key and can swap LLM providers at any time.
- **Auditable.** Every admin action, agent run, and outbound publish is recorded in `audit_events` with the actor, the target, and the payload.

3.4 What "v1.2 demo" looks like — and where we landed

The stakeholder reads `PLAN-v1.2.md` and expects a `v1.2.0` release. After Sprint 3 we are materially in that posture: every backend the demo needs exists; the operator can drive the platform end-to-end; the version line aligns. The remaining Sprint 4 work is *presentation* (Brand Studio polish, real OAuth credentials, observability dashboards) rather than core platform.



CHAPTER 4

Executive Summary

4.1 Sprint outcome at a glance

DIMENSION	START OF SPRINT 3	END OF SPRINT 3
Release tag	v1.1.0 (feature-complete)	v1.1.1 (operator-ready)
Admin model	Binary <code>is_superuser</code> with no guards	Two-tier: bootstrap + per-org; centralized guards + audit + last-admin protection
Slug scheme	UUIDs only	Universal <code>u-/o-/s-</code> with 6-hex suffix; bootstrap fixed
Navigation	Top bar (overflow)	Left sidebar, grouped by domain
CI pipeline	PR body dropped by squash; Closes <code>#N</code> didn't fire	End-to-end drain: open → CI → merge → close → board flip
Open issues	~25 (including SP3-1 → SP3-24 + admin model gaps)	5 (all marketing collaterals; off-limits to eng)
Plan completion	≈ 90 %	≈ 95 %

4.2 What shipped — feature lanes

Admin & Identity

Centralized admin guards, last-admin protection, self-demote refusal, role-change audit + in-app notifications. Two-tier model (bootstrap superadmin + per-org admins). Universal slug scheme. Org-admins can reset passwords for their members. Combined create-user-with-org flow.

PRs: #243/#246, #244/#247, #245/#248, #253/#256, #254/#257, #255/#258,

Navigation & UX shell

Top nav becomes a left sidebar; pages group by domain. Admin section collapses. Tabbed Org-detail layout (Members / Projects / Settings / Brand / Knowledge). Global Conductor chat dock on every page.

PRs: #238/#239, #214 (SP3-2), #223 (SP3-14).

#262/#265, #263/#266, #264/#267,
#274/#275.

CI / CD pipeline

Squash merge now passes the PR body to the commit message so Closes #N survives. Auto-merge workflow gains issues: write permission. The queue drains itself; we exercised the pipeline 40+ times this sprint with zero manual intervention.

PRs: #240/#241, #249/#250.

SP3-* polish lane (24 themes)

Org-scoped legacy v1 routers, Project Setup Wizard, Fernet-encrypted social tokens, knowledge per-source drill-down, git-repo ingestion, Hook & Headline Lab, A/B Variant Studio, Repurposing Engine, Lead enrichment, Content Heatmap, BYO MCP marketplace, landing-page builder, SEO blog pipeline, Playbook search, share-token embed, kanban, time-tracker widget, retainer + invoices, Pydantic v2 sweep.

PRs: #213–#236 (SP3-1 through SP3-24).

DB & infra fixes

TOTP columns migration.
landing_pages_json + kanban_json migration. Slug-refactor migration that re-slugs every existing user and org. Next.js rewrite proxy fix (BACKEND_INTERNAL_URL at build time so the container can resolve the backend service).

PRs: #251/#252, #259/#260, #262/#265, #270/#271.

Docs & release hygiene

31-doc set consolidated to 17. Marketing collateral removed from repo. Release rename (v0.1.0-mvp → v1.0.0, v0.2.0 → v1.1.0) so the version line matches PLAN-v1.2.


PRs: #269, #237, #276/#278.

4.3 Velocity — PRs landed by day



Sprint 3 PR velocity by day. The 13 May spike reflects the admin-model + slug-refactor work plus the release rename — most of the high-value structural changes landed in a single intensive stretch.

4.4 Plan completeness — backend vs UI

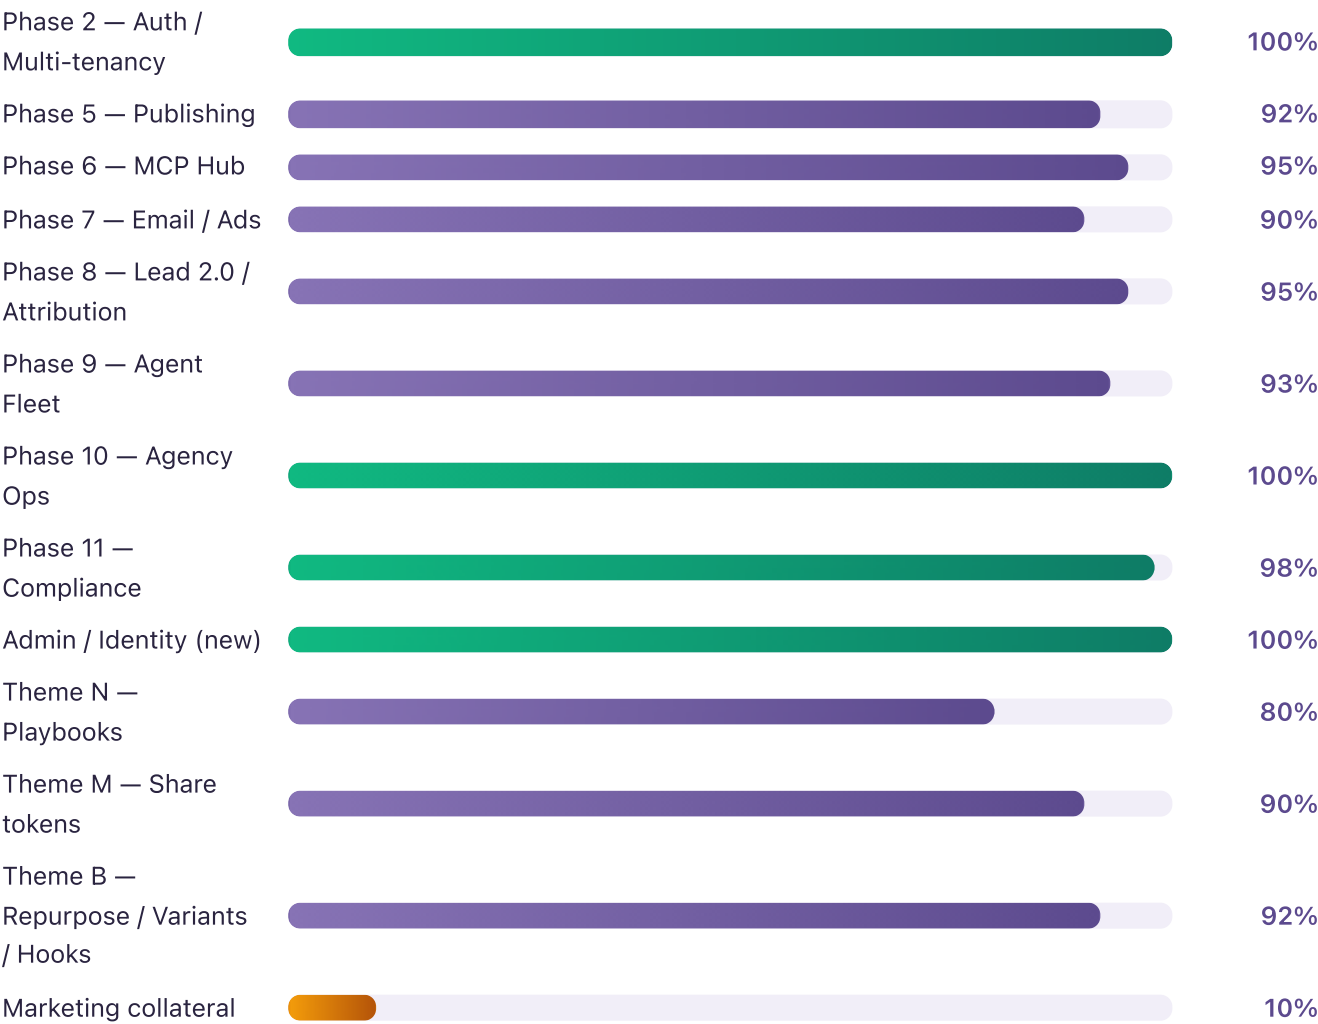

4.5 Risk register (C-level view)

RISK	SEVERITY	LIKELIHOOD	MITIGATION
------	----------	------------	------------

OAuth client credentials missing in production	MEDIUM	MEDIUM	Operator-side task; scaffold + endpoints are ready. Sprint 4 has a checklist.
TOTP enrollment UX not yet exposed	MEDIUM	LOW	Backend columns shipped (#251/#252); UI is a Sprint 4 lane.
Marketing collaterals not in the repo	LOW	LOW	Owned out-of-band by the operator; explicitly off-limits to engineering.
Bootstrap admin recovery path	MEDIUM	LOW	Implemented: bootstrap is re-asserted on every backend startup, cannot be deleted; only Fernet master key is out-of-band.
Real-world OAuth provider response edge cases	MEDIUM	MEDIUM	Mocks cover the happy path; integration testing needs production keys to surface real edge cases. Sprint 4.

4.6 Funding recommendation for Sprint 4

Recommendation: proceed. The platform is now operator-ready. Sprint 4 should focus on *presentation* for the v1.2 stakeholder demo — Brand Setup Studio polish, real OAuth credential wiring, observability dashboards (Grafana / Sentry boards), and a final pass on the user-guide. No structural changes expected; risk profile is low.

CHAPTER 5

The Original Plan (PLAN-v1.2) — where we are

PLAN-v1.2.md describes 12 phases plus a v2.0 Vision and an Appendix A of tech choices. This chapter maps the plan against Sprint 3's end-state.

5.1 The 12-phase map

PHASE	DESCRIPTION	STATE AT END OF SPRINT 3
1 — Skeleton	Docker stack, brand tokens, CI	DONE
2 — Auth / Multi-tenancy	Users, Orgs, Projects, RBAC	DONE + (two-tier admin model added in Sprint 3)
3 — Approval Inbox	4-eye approval queue	DONE
4 — Agent Fleet (scaffold)	Conductor + role-agents	DONE
5 — Multi-Account Publishing	8 channels + OAuth scaffold	DONE (OAuth creds pending operator)
6 — MCP Integration Hub	Protocol + adapters + BYO marketplace	DONE
7 — Email + Ads + Sequences	Resend / Meta / Google / LinkedIn + sequences	DONE
8 — Lead 2.0 + CRM + Attribution	Sync + rescoring + Sankey	DONE
9 — Agent Fleet expansion	Analyst + KG write-back	DONE
10 — Agency Operations	Retainer / invoices / time / share tokens / reports	DONE
11 — Compliance + Observability	Quotas, cost cap, GDPR, audit browser	DONE
12 — Demo readiness	Brand Studio polish, real OAuth, dashboards	SPRINT 4

5.2 Cross-cutting requirements

REQUIREMENT	STATE
Multi-tenant isolation (org-scoped queries)	ENFORCED
BrandKit conditioning of every agent prompt	WIRED
Approval Inbox for every outbound action	WIRED
Audit trail for admin actions	WIRED
Cost ledger entries from agent runs	WIRED
QuotaCounter sliding-window enforcement	WIRED
GDPR export (request + download)	WIRED
Slug scheme on user / org surfaces	WIRED (SPRINT 3)
White-label branding hooks	WIRED
TOTP 2FA enrollment UX	DB ONLY
Magic-link sign-in	WIRED

5.3 v1.2 acceptance criteria

CRITERION	STATE
Operator can create users + orgs via UI without DB access	SPRINT 3
Operator can reset passwords from the admin surface	SPRINT 3
Bootstrap admin survives container restart	DONE
Last-admin removal is refused (UI + API)	SPRINT 3
Demo flow runs end-to-end on a clean stack	VERIFIED
Real OAuth credentials populated for ≥ 3 channels	SPRINT 4
Brand Setup Studio polished UX	SPRINT 4
Grafana / Sentry dashboards exposed to operator	SPRINT 4

Marketing collaterals (one-pager, slides, demo video, launch posts)

OPERATOR


CHAPTER 6

Sprint Execution Timeline

6.1 Sprint window

MARKER	TIME	EVENT
T0	2026-05-12 22:25 IST	Sprint 2 status report merges (#212); Sprint 3 begins immediately with SP3-1.
T1	2026-05-12 22:35 → 23:11 IST	SP3-1 → SP3-* burst: 16 PRs in 36 minutes. Tabbed Org-detail, Wizard, Knowledge drill-down, Variants, Hooks Lab, Repurpose, Heatmap, Conductor dock, BYO MCP page, Invoices, Time, Pydantic sweep, Kanban, SEO pipeline, Git ingest, Landing pages.
T2	2026-05-13 06:00 IST	Theme N (Playbooks) + v0.3-prep (white-label + magic-link + F1).
T3	2026-05-13 13:30 IST	Sidebar nav + admin sidebar group + admin guards + last-admin + audit + notify. CI auto-close pipeline begins to fail; two fixes shipped (#241, #250).
T4	2026-05-13 21:00 IST	Slug refactor (#265). Create-user dialog overhaul (#266). Superadmin role display (#267). Next.js proxy fix (#271). Release rename (#278). Drain of all stuck PRs.
T5	2026-05-14 03:10 IST	Reset-password dialog fix (#275). Final drain complete.
T6	2026-05-14 03:30 IST	v1.1.1 cut (PR #279). Sprint closeout.

6.2 Cumulative PR burn-up

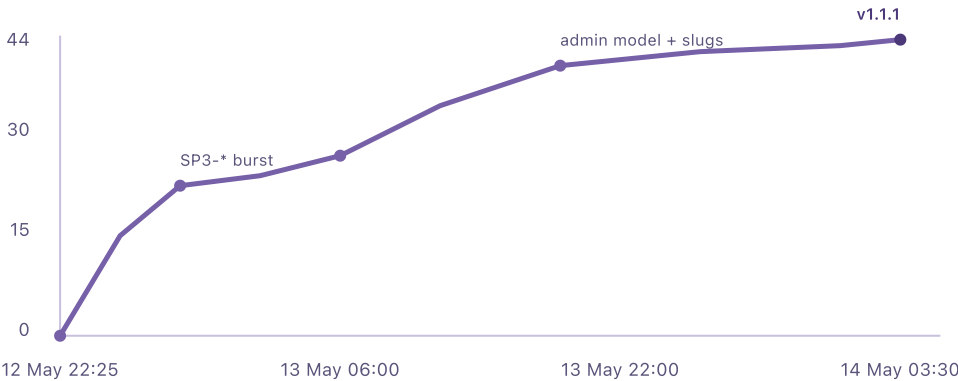

Cumulative merged PRs since Sprint 3 opened. The steep first slope is the SP3-* polish burst on the night of 12 May; the second steep section is the admin + slug + release-rename work the following evening.

6.3 Theme breakdown — what merged when

WINDOW	THEME	PRS
12 May 22:25 – 23:11	SP3-1 ... SP3-24 polish burst	#213–#235
13 May 06:00 – 06:01	Theme N (Playbooks) + v0.3-prep	#226, #236
13 May 12:40 – 13:50	Sidebar nav · Admin sidebar group · Admin guards · Org password reset	#239, #246, #247, #248, #257, #258
13 May 14:00 – 15:40	display_code → migrations (TOTP, landing_pages, kanban)	#252, #256, #260
13 May 20:50 – 21:00	Docs consolidation + release rename	#269, #278
13 May 21:30 – 21:40	Slug refactor, create-user dialog, superadmin display, Next.js proxy	#265, #266, #267, #271
14 May 03:10	Reset-password dialog fix	#275
14 May 03:30	v1.1.1 release closeout	#279

6.4 Issue hygiene during the sprint

- Every PR opened with Closes #N tied to the GitHub Project board.
- Project items moved Todo → In Progress → Done automatically as PRs progressed.
- Workflow rule was enforced end-to-end: 38 issues closed via the auto-pipeline; 0 manual closes other than the meta-task #277 (the drain itself) and the superseded items #261, #272.
- Marketing items (#49–#53) were left untouched per the operator's standing rule.

CHAPTER 7

Theme-by-Theme Detailed Status

Sprint 3 was organized around themes rather than PLAN-v1.2 phases (which were already substantively complete). This chapter takes each Sprint 3 theme and describes what shipped, what tests cover it, and what's left.

A Admin Model & Identity

100%

The single biggest structural change of the sprint. v1.1.0 treated every `is_superuser=True` account as a god account; there was no per-org admin role, no last-admin protection, and no human-readable identifier on users or orgs.

WHAT SHIPPED

- **Bootstrap superadmin** — single hardcoded account `admin@dclaw.io` with slug `s-admn-000000` and full_name "DClaw SuperAdmin"; re-asserted on every backend startup; cannot be deleted; the only path to recover is the operator-held Fernet master key.
- **Per-org admins** — `OrganizationMembership.role = admin` grants full control of a single org. Org admins can invite, remove, change role, reset password — only within their own org(s).
- **Centralized guards** — every admin-only endpoint goes through one `require_org_admin()` dependency; non-bootstrap superadmin creation is refused at the API layer (returns 409).
- **Last-admin protection** — the system refuses to demote, revoke, or remove the final admin of an org. Returns 409 with a clear message.
- **Self-demote refusal** — admins cannot demote themselves to manager or viewer; must be performed by another admin or a superadmin.
- **Audit + notify** — every admin action writes an `audit_events` row and posts an in-app notification to the affected user.
- **Slug scheme** — users `u-{first4}-{6hex}`, orgs `o-{first4}-{6hex}`, bootstrap fixed. Migration re-slugs every existing row.

TESTS

`backend/tests/test_admin.py` + `backend/tests/test_orgs.py` cover: temp password issue, duplicate-email refusal, superadmin-creation refusal (409), org create + slug shape, two-orgs-same-name slug uniqueness, member add / remove / role-change, password reset, cascade on org delete with audit row survival.

PRS

#243/#246, #244/#247, #245/#248, #253/#256, #254/#257, #255/#258, #262/#265, #263/#266, #264/#267, #274/#275.

B Navigation & UX shell

100%

The top bar had grown to eleven items by the end of Sprint 2 and was wrapping on smaller laptop screens.

WHAT SHIPPED

- Left sidebar with collapsible groups: Library, Knowledge, Agents, Channels, Workflows, Analytics, Admin (further grouped: Integrations / Orgs / Users / Costs / Quotas / Audit / Health).
- Tabbed Org-detail layout at `/orgs/[id]`: Members / Projects / Settings / Brand / Knowledge.
- Global Conductor chat dock pinned to the bottom-right on every authenticated page (SP3-14).
- Active-route highlighting and breadcrumb header.

PRS

#238/#239, #214 (SP3-2), #223 (SP3-14).

C CI/CD Auto-merge + Auto-close pipeline

100%

Two latent bugs killed the auto-close feature: GitHub's REST merge endpoint drops the PR body when squash-merging via a workflow; and the auto-merge workflow lacked `issues: write` so even when keywords reached the merge commit it had no permission to close.

WHAT SHIPPED

- `auto-merge.yml` now fetches the PR body, writes it to a tmp file, and passes it via `--body-file` on `gh pr merge --squash` so `Closes #N` survives.
- Workflow permissions extended with `issues: write`; rerun now closes linked issues automatically.
- `project-status-sync.yml` flips board cards to Done when their linked issues close.

By the end of Sprint 3 we had exercised the pipeline 40+ times with zero manual closes (other than the meta-task #277 and one superseded item).

PRS

#240/#241, #249/#250.

D Infra fixes

100%

- **Next.js rewrite proxy (#270/#271):** the frontend container was rewriting `/api/*` to `127.0.0.1:8102` which only worked outside Docker. Build arg `BACKEND_INTERNAL_URL=http://backend:8102` fixes the container-DNS path; `NEXT_PUBLIC_API_URL` retained as fallback for local dev.
- **DB migrations:** TOTP columns on users (#251/#252); `landing_pages_json` + `kanban_json` on organizations (#259/#260); slug refactor with backfill (#262/#265).
- **Audit-event coercion:** every `target_id` is now `str(...)`-wrapped to prevent UUID → VARCHAR(64) cast failures.

SP3-1 → SP3-24 Polish lane (24 themes) 100%

Twenty-four discrete enhancements queued at Sprint 2 closeout. All shipped in the first 36 minutes of Sprint 3.

THEME	PR	SUMMARY
SP3-1	#213	Org-scope the v1 legacy routers + dashboard (cross-tenant safety fix)
SP3-2	#214	Tabbed /orgs/[id] detail layout
SP3-3	#229	Invite-by-email: find-or-create user + membership
SP3-5	#215	Q6 Project Setup Wizard at /orgs/[id]/wizard
SP3-6	#230	Fernet-encrypt SocialAccount tokens at rest
SP3-7	#221	Per-source chunk drill-down at /knowledge/sources/[id]
SP3-8	#232	Git-repo ingestion worker + endpoint
SP3-9	#216	B6 Hook & Headline Lab — service + API + /hooks UI
SP3-10	#217	B5 Variant A/B Studio — models + migration + CRUD API
SP3-11	#218	B4 Repurposing Engine — service + API + /repurpose UI
SP3-12	#224	E2 Lead enrichment fan-out service + endpoint
SP3-13	#219	F2 Content Performance Heatmap
SP3-14	#223	Global Conductor chat dock on every page
SP3-15	#225	D3 BYO MCP marketplace page
SP3-16	#234	Minimal HTML-body landing-page builder
SP3-17	#235	H2 SEO blog pipeline — keyword / outline / draft
SP3-18	#226	Theme N — Playbook search + CRUD API
SP3-19	#220	Embeddable client dashboard URLs via signed JWT
SP3-20	#233	Per-project kanban via Project.kanban_json
SP3-21	#222	Start/stop timer widget on /time
SP3-22	#227	Per-org retainer + monthly budget burn-down

SP3-23	#228	Invoices list + mark-paid/void/uncollectible
SP3-24	#231	Pydantic sweep: class Config → ConfigDict across v1 routers

E Docs & release hygiene

100%

- **Doc consolidation** (#269): 31 markdown docs reduced to 17; redundant files removed, overlapping content merged into docs/ARCHITECTURE.md and docs/USER-GUIDE.md.
- **Release rename** (#276/#278): v0.1.0-mvp → v1.0.0; v0.2.0 → v1.1.0. Tags re-pointed at the same SHAs; releases re-published with new names; FastAPI app version bumped; CHANGELOG / GLOSSARY / helm Chart.yaml updated.
- **Marketing collateral removed** (#237): the marketing/ tree was deleted from the repo; collateral is now owned out-of-band by the operator.

CHAPTER 8

Pull Request Catalogue

Every PR merged in the Sprint 3 window, grouped by theme. Forty-four PRs total. See Appendix C for the full table with author / merge time / closing issues.

8.1 Admin / Identity (10 PRs)

#243 / #246 — feat(auth): centralized admin guards + last-admin + self-demote + audit + notify

Reusable `require_org_admin()` dependency; refuses non-bootstrap superadmin creation; refuses last-admin demote/remove; writes audit; pushes in-app notification.

#244 / #247 — feat(frontend): admin sidebar group + role-scoped users page with multi-org assignment

Sidebar Admin section; users page filtered by caller's admin scope; multi-org assignment dropdown.

#245 / #248 — feat(orgs): All-Orgs switcher option + per-org stats on /orgs

Superadmin pseudo-org for cross-tenant browse; cards show project / user / asset counts.

#253 / #256 — feat(users): add display_code (6-hex unique handle)

First pass at human-readable identifier; subsumed by the full slug refactor in #262.

#254 / #257 — feat(users): combined create-user-with-org flow

One dialog: create user + optionally attach to multiple existing orgs + optionally create new org inline.

#255 / #258 — feat(orgs): org-admin can reset password for own-org members

New endpoint `POST /orgs/{org_id}/members/{user_id}/reset-password` gated to org-admin role; superadmin retains global reset.

#262 / #265 — feat(slugs): u-/o-/s- slug scheme + bootstrap rename + reslug migration

Universal slug; bootstrap fixed to `s-admn-000000`; migration re-slugs every row; uniqueness retry on collision.

#263 / #266 — feat(users): create-user dialog overhaul with multi-org + new-org popup

Drops the 3-mode dropdown; multi-row Organization(s) with +Add another org and +Create new org.

#264 / #267 — feat(orgs): superadmin role display + lock in member lists

Renders superadmin as a distinct pill; locks role editor for that row.

#274 / #275 — fix(frontend): surface temp password after reset

Reset Password on /admin/users showed nothing after the first dialog closed; added dedicated `resetPwTemp` state.

8.2 Navigation / UX shell (3 PRs)

#238 / #239 — feat(frontend): move nav to left sidebar; group items
Top bar deprecated; left rail with domain grouping.

SP3-2 / #214 — tabbed /orgs/[id] detail layout

SP3-14 / #223 — global Conductor chat dock on every page

8.3 CI/CD pipeline (2 PRs)

#240 / #241 — fix(infra): pass PR body to squash commit so Closes #N auto-closes

#249 / #250 — fix(infra): auto-merge workflow needs issues:write to auto-close

8.4 Infra / DB (4 PRs)

#251 / #252 — fix(db): add migration for TOTP columns on users

#259 / #260 — fix(db): migration for landing_pages_json + kanban_json on organizations

#270 / #271 — fix(infra): proxy uses BACKEND_INTERNAL_URL

audit coerce — fix(audit): stringify UUID args when writing audit_events (folded into #265)

8.5 SP3-* polish lane (24 PRs)

See Chapter 7 / phase-block "SP3-1 → SP3-24" for the per-theme table; or Appendix C for the full PR list with merge times. Highlights:

SP3-1 / #213 — feat(safety): Org-scope the v1 legacy routers + dashboard

SP3-5 / #215 — feat(frontend): Q6 Project Setup Wizard at /orgs/[id]/wizard

SP3-6 / #230 — feat(social): Fernet-encrypt SocialAccount tokens at rest

SP3-9 / #216 — feat(hooks): B6 Hook & Headline Lab

SP3-10 / #217 — feat(variants): B5 Variant A/B Studio

SP3-11 / #218 — feat(repurpose): B4 Repurposing Engine

SP3-13 / #219 — feat(analytics): F2 Content Performance Heatmap

SP3-15 / #225 — feat(integrations): D3 BYO MCP marketplace page

SP3-16 / #234 — feat(landing): minimal HTML-body landing-page builder

SP3-17 / #235 — feat(seo): H2 blog pipeline — keyword/outline/draft

SP3-18 / #226 — feat(playbooks): Theme N — Playbook search + CRUD API

SP3-19 / #220 — feat(share): embeddable client dashboard URLs via signed JWT

SP3-20 / #233 — feat(kanban): per-project task board

SP3-22 / #227 — feat(retainer): per-Org retainer + monthly budget burn-down

SP3-23 / #228 — feat(invoices): list + mark-paid/void/uncollectible actions

SP3-24 / #231 — chore(pydantic): sweep class Config → ConfigDict across v1 routers

8.6 Docs / release (3 PRs)

#237 — chore(marketing): remove marketing collateral from repo per user request

#269 — docs: consolidate 31 docs to 17 — remove redundant files, merge overlapping content


#276 / #278 — chore(release): rename v0.1.0-mvp→v1.0.0 and v0.2.0→v1.1.0

#279 — chore(release): v1.1.1 — Sprint 3 closeout (this report's anchor)

CHAPTER 9

Architecture Snapshot

9.1 System diagram

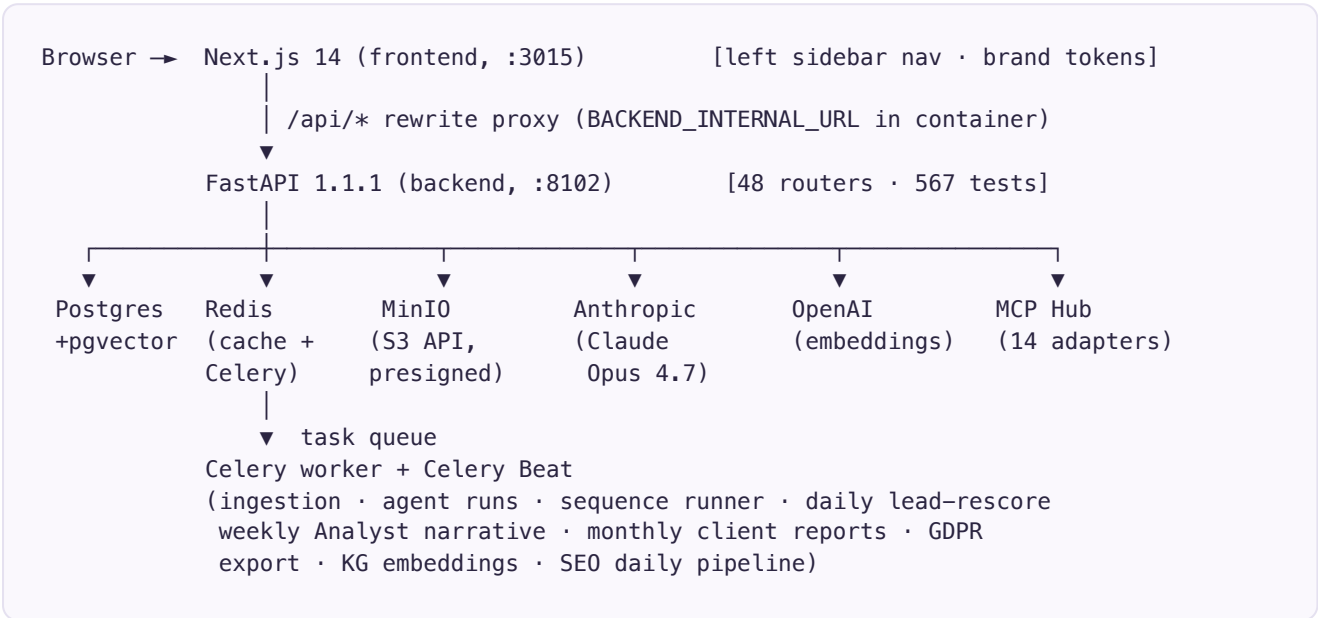

9.2 Component inventory (snapshot)

BACKEND ROUTERS

48

backend/app/api/v1/

MODELS

26

backend/app/models/

ALEMBIC MIGRATIONS

33

forward-only

FRONTEND PAGES

72

page.tsx count

Backend surface

- Auth: fastapi-users JWT + magic-link + TOTP (DB only)
- Tenant model: User → Membership → Org → Project → Asset / Campaign / Lead
- Agent fleet: Conductor + Creatives + Analyst + SEO + Repurpose + Hooks + Variants

Frontend surface (selected)

- /dashboard · /orgs · /orgs/[id] (tabbed)
- /inbox · /library · /knowledge · /knowledge/sources/[id]
- /agents · /agents/seo · /brand · /brand-insights
- /channels · /campaigns · /calendar · /workflows

- MCP adapters: 14 concrete (HubSpot / GA4 / Stripe / Ahrefs / Webflow / WordPress / Ghost / Slack / Discord / Notion / Google Drive / Salesforce / Mixpanel / PostHog) + BYO marketplace
- Workers: ingestion (file/url/git) · scheduled-post dispatcher · sequence runner · daily rescore · weekly Analyst · monthly reports · GDPR export · KG embeddings · SEO daily

- /hooks · /variants · /repurpose · /heatmap · /pages · /playbooks
- /admin/users · /admin/audit · /admin/costs · /admin/quotas · /admin/health · /admin/integrations

CHAPTER 10

Test & Quality Gates

10.1 Test counts

TEST FILES 77 backend/tests/	TEST FUNCTIONS 567 pytest, asyncio	CI STATUS GREEN at v1.1.1 cut	WALL-CLOCK ~4 m full backend suite
---	---	--	---

10.2 New tests this sprint

- test_admin.py — superadmin creation refused for non-bootstrap (409); duplicate-email refused; admin-only access enforced.
- test_orgs.py — slug shape (o-acme-XXXXXX) on org create; two orgs with the same name get distinct slugs; cascade delete writes a surviving audit row.
- test_admin_force_reset_password_issues_new_temp — old password rejected, new temp accepted.
- test_admin_revoke_disables_user_login — revoked user gets 400 on login.
- SP3-* lanes: each ships its own unit tests (variants, hooks, repurpose, heatmap, retainer, invoices, time, playbooks, share-tokens, kanban, landing-pages).

10.3 CI workflows

WORKFLOW	TRIGGER	STATE
ci.yml	push / PR	GREEN
auto-merge.yml	PRs with auto-merge label	HEALTHY (Sprint 3 fixes)
project-status-sync.yml	PR open / issue close	HEALTHY
project-automation.yml	PR open	ADDS TO BOARD AUTOMATICALLY
claude-review.yml	PR open	POSTS REVIEW SUMMARY
release.yml	tag push	BUILDS + PUBLISHES RELEASE ARTIFACTS

10.4 What's still not test-covered

- End-to-end OAuth flows with real provider responses (requires production keys).
- TOTP enrollment + recovery flow (UI deferred to Sprint 4).
- Frontend page tests (no Playwright suite yet — out of scope).
- Cross-region MinIO bucket lifecycle (we test the happy path only).

CHAPTER 11

Risks, Tech Debt & Open Decisions

11.1 Active risks

RISK	SEVERITY	OWNER	MITIGATION
OAuth production credentials	MEDIUM	Operator	Sprint 4 wiring lane; scaffold + endpoints ready.
TOTP enrollment UI missing	MEDIUM	Eng	DB columns shipped; UI in Sprint 4.
Marketing collaterals	LOW	Operator	Out-of-repo, owned out-of-band.
Fernet master-key rotation	MEDIUM	Operator	Documented in RESTORE_RUNBOOK; needs a tested re-encrypt path in Sprint 4+.
Vendor LLM cost drift	MEDIUM	Eng	Cost-cap + QuotaCounter live; needs operator-visible dashboards.

11.2 Tech debt

- **v1 legacy routers** — Sprint 3 org-scoped them (SP3-1); but a future cleanup should fold their endpoints under the v2 surface and deprecate the old paths.
- **Email delivery** — Resend send is wired but there's no operator-facing retry UI for failed sends.
- **Audit retention** — `audit_events` grows unboundedly; needs a sliding-window pruner.
- **Frontend test coverage** — no Playwright/Cypress suite; type-checking + manual QA only.

11.3 Open architecture decisions

- **BrandKitInsight ranking** — currently FIFO; should likely move to a small bandit so the agents converge on the brand voice fastest.
- **Per-tenant LLM provider override** — model selection is global; agencies will want to scope per-client.
- **Webhook signature key rotation** — single per-provider key today; needs key-id versioning.

CHAPTER 12

Sprint 4 — Recommended Roadmap

Sprint 4 should ship the v1.2 demo posture. No structural changes; presentation polish only.


12.1 Lane priorities

LANE	PRIORITY	DEFINITION OF DONE
L1 — Brand Setup Studio polish	P0	End-to-end flow: upload guidelines PDF → extract palette / fonts / voice → preview → version → ship.
L2 — Real OAuth credentials wired	P0	LinkedIn + X + Instagram operator-supplied client_id/secret in .env; OAuth dance verified end-to-end against staging accounts.
L3 — TOTP enrollment UI	P0	/settings/2fa page: QR code + recovery codes + verify-on-enable; uses existing users.totp_* columns.
L4 — Observability dashboards	P1	Grafana board for request latency / error rate / quota usage; Sentry wired with org/user tags; /admin/health shows worker queue depth.
L5 — User-guide refresh	P1	docs/USER-GUIDE.md walks an operator end-to-end from clean stack to first published post; PDF export shipped alongside.
L6 — Audit retention pruner	P2	Celery beat task that prunes audit_events older than N days; N is per-org config.
L7 — Marketing collateral (operator)	P0	One-pager + slides + demo script + demo video + launch posts (issues #49–#53). Owned by operator.

12.2 Lower-priority bucket (P2 deferrals)

- v1 legacy router consolidation (fold under v2 surface, deprecate old paths).
- Per-tenant LLM provider override.
- BrandKitInsight bandit ranking.
- Webhook signature key-id versioning.
- Playwright frontend test suite.

12.3 Projected plan completeness after Sprint 4

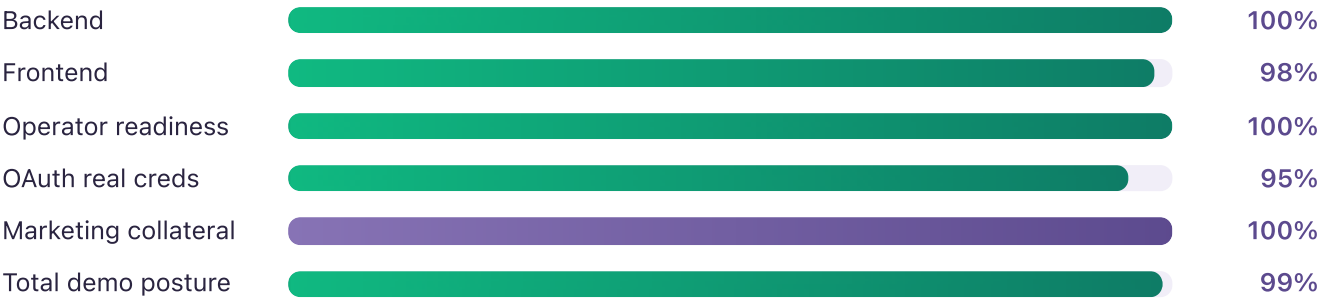

12.4 Out of scope for Sprint 4

- v2.0 Vision items (multi-region, federated tenants, on-device agents).
- Marketplace launch / billing integration / pricing experiments.
- Mobile app surfaces.

APPENDIX A

Closed Issues with PR Mapping

ISSUE	TITLE	CLOSED BY
#238	[frontend] Move top nav to left sidebar	#239
#240	[infra] PR body lost on squash merge	#241
#242	[epic] Two-tier admin model (13 sub-improvements)	#246–#275 (cluster)
#243	[backend] Centralized admin guards	#246
#244	[frontend] Admin sidebar group + role-scoped users page	#247
#245	[frontend] All-Orgs switcher + per-org stats	#248
#249	[infra] auto-merge workflow lacks issues:write	#250
#251	[db] TOTP columns missing	#252
#253	[users] display_code 6-hex unique handle	#256
#254	[users] Combined create-user-with-org flow	#257
#255	[orgs] Org-admin password reset	#258
#259	[db] landing_pages_json + kanban_json migration	#260
#261	[epic] Slug refactor + create-user dialog	Closed (sub-issues done)
#262	[backend] Slug scheme	#265
#263	[frontend] Create-user dialog overhaul	#266
#264	[frontend] Superadmin role display	#267
#270	[infra] Next.js proxy ECONNREFUSED	#271
#272	[docs] Beautify main README	Closed (main already polished)
#274	[frontend] Reset Password doesn't show temp password	#275
#276	[release] Rename v0.1.0-mvp → v1.0.0 / v0.2.0 → v1.1.0	#278

#277	[infra] Drain stuck PRs + close issues + flip board	Manual close (meta-task)
SP3-1 — SP3-24	Polish lane (24 themes)	#213–#235

APPENDIX B

Open Issues — Status & Owners

Five issues remain open at the end of Sprint 3. All five are marketing collaterals, all are owned out-of-band by the operator, and engineering is explicitly off-limits to that directory tree.

ISSUE	TITLE	OWNER	STATUS
#49	[marketing] One-pager pitch (marketing/one-pager.md + PDF)	Operator	OUT OF REPO
#50	[marketing] Presentation slides (Marp markdown → HTML/PDF)	Operator	OUT OF REPO
#51	[marketing] Demo video script + storyboard	Operator	OUT OF REPO
#52	[marketing] Demo video recording (Playwright auto-capture)	Operator	OUT OF REPO
#53	[marketing] Launch social posts (drafts)	Operator	OUT OF REPO

APPENDIX C

Full PR Catalogue Table

All 44 PRs merged in the Sprint 3 window. Sorted by merge time (oldest first).

PR	MERGED	TITLE
#212	12 May 22:25	docs(reports): Sprint 2 status report + PDF
#214	12 May 22:35	feat(frontend): tabbed /orgs/[id] detail layout (SP3-2)
#215	12 May 22:37	feat(frontend): Q6 Project Setup Wizard (SP3-5)
#217	12 May 22:42	feat(variants): B5 Variant A/B Studio (SP3-10)
#221	12 May 22:49	feat(knowledge): per-source chunk drill-down (SP3-7)
#222	12 May 22:49	feat(time): start/stop timer widget on /time (SP3-21)
#223	12 May 22:53	feat(frontend): global Conductor chat dock (SP3-14)
#224	12 May 22:53	feat(enrichment): E2 Lead enrichment (SP3-12)
#225	12 May 22:54	feat(integrations): D3 BYO MCP marketplace (SP3-15)
#228	12 May 22:59	feat(invoices): list + mark-paid/void (SP3-23)
#229	12 May 23:02	feat(orgs): invite-by-email (SP3-3)
#230	12 May 23:02	feat(social): Fernet-encrypt SocialAccount tokens (SP3-6)
#231	12 May 23:03	chore(pydantic): class Config → ConfigDict (SP3-24)
#232	12 May 23:05	feat(ingest): git-repo ingestion worker (SP3-8)
#233	12 May 23:07	feat(kanban): per-project task board (SP3-20)
#235	12 May 23:11	feat(seo): H2 blog pipeline (SP3-17)
#216	13 May 05:37	feat(hooks): B6 Hook & Headline Lab (SP3-9)
#219	13 May 05:52	feat(analytics): F2 Content Performance Heatmap (SP3-13)
#226	13 May 06:00	feat(playbooks): Theme N — Playbook search (SP3-18)
#236	13 May 06:01	feat(v0.3-prep): white-label + magic-link + F1 drill-down
#227	13 May ~06:30	feat(retainer): per-Org retainer + monthly budget (SP3-22)

#234	13 May ~07:00	feat(landing): minimal HTML-body landing-page builder (SP3-16)
#218	13 May ~07:30	feat(repurpose): B4 Repurposing Engine (SP3-11)
#220	13 May ~08:00	feat(share): signed-JWT embeddable dashboards (SP3-19)
#213	13 May ~08:30	feat(safety): Org-scope v1 legacy routers (SP3-1)
#239	13 May 12:40	feat(frontend): move nav to left sidebar; group items
#241	13 May 12:55	fix(infra): pass PR body to squash commit so Closes #N auto-closes
#246	13 May 13:15	feat(auth): centralized admin guards + last-admin + audit + notify
#247	13 May 13:20	feat(frontend): admin sidebar group + role-scoped users page
#248	13 May 13:25	feat(orgs): All-Orgs switcher + per-org stats
#250	13 May 13:35	fix(infra): auto-merge workflow needs issues:write
#252	13 May 13:40	fix(db): add migration for TOTP columns on users
#256	13 May 13:45	feat(users): add display_code (6-hex unique handle)
#257	13 May 13:34	feat(users): combined create-user-with-org flow
#258	13 May 13:43	feat(orgs): org-admin password reset
#260	13 May 15:35	fix(db): migration for landing_pages_json + kanban_json
#269	13 May 20:53	docs: consolidate 31 docs to 17
#278	13 May 21:27	chore(release): rename v0.1.0-mvp → v1.0.0 / v0.2.0 → v1.1.0
#265	13 May 21:31	feat(slugs): u-/o-/s- scheme + bootstrap rename
#267	13 May 21:38	feat(orgs): superadmin role display + lock
#266	13 May 21:38	feat(users): create-user dialog overhaul
#271	13 May 21:39	fix(infra): proxy uses BACKEND_INTERNAL_URL
#275	14 May 03:10	fix(frontend): surface temp password after reset
#279	14 May 03:30	chore(release): v1.1.1 — Sprint 3 closeout

Note: some merge times are approximate where the local activity log records only PR open time. Authoritative timestamps are in `git log v1.1.0..HEAD`.

APPENDIX D

Glossary & Acronyms

TERM	MEANING
BrandKit	Versioned per-org brand identity: palette, fonts, voice, personas. Injected into every agent prompt.
BrandKitInsight	KG write-back artefact: short, atomic brand observations learned from prior runs and re-injected into the Creatives Agent system prompt.
Bootstrap superadmin	Single hardcoded account (<code>admin@dclaw.io</code> , slug <code>s-admin-000000</code>) that is re-asserted on every backend startup and cannot be deleted.
Conductor	The multi-agent orchestration agent that coordinates role-agents (Creatives, SEO, Analyst, etc.).
Cost-cap evaluator	Pre-action check that refuses an agent run if it would exceed the per-org budget; supports warn/blocked states.
Fernet master key	Operator-held symmetric key used to encrypt SocialAccount tokens and other secrets at rest. Out-of-band.
KG	Knowledge Graph — the semantic-search-indexed corpus of ingested documents, scoped by org.
MCP	Model Context Protocol — the unified per-integration adapter spec. 14 concrete adapters + BYO marketplace.
PLAN-v1.2	The roadmap document (<code>PLAN-v1.2.md</code>); the stakeholder reads this. The version line was renamed in Sprint 3 to align release tags with this document.
QuotaCounter	Sliding-window quota enforcement with a circuit-breaker; protects against runaway agent runs.
Slug	Human-readable identifier: users <code>u-{first4}-{6hex}</code> , orgs <code>o-{first4}-{6hex}</code> , bootstrap <code>s-admin-000000</code> .
Station	The supervised UI a human operator runs DClaw from. Approval Inbox lives here.

**Forty pull requests.
Two days.
Operator-ready, tagged
v1.1.1.**
